
PLAN VIEW
COMPU-LOG DEVIATION

CLIENT: ATRUM COAL
LOCATION: GROUNDHOG
HOLE ID: DHGH-14-20
DATE OF LOG: 06/24/14
PROBE: 9411A 4504

MAG DECL: 19.5

SCALE: 2 M/CM
TRUE DEPTH: 47.43 M
AZIMUTH: 228.8
DISTANCE: 14.9 M
+ = 5 M INCR
○ = BOTTOM OF HOLE

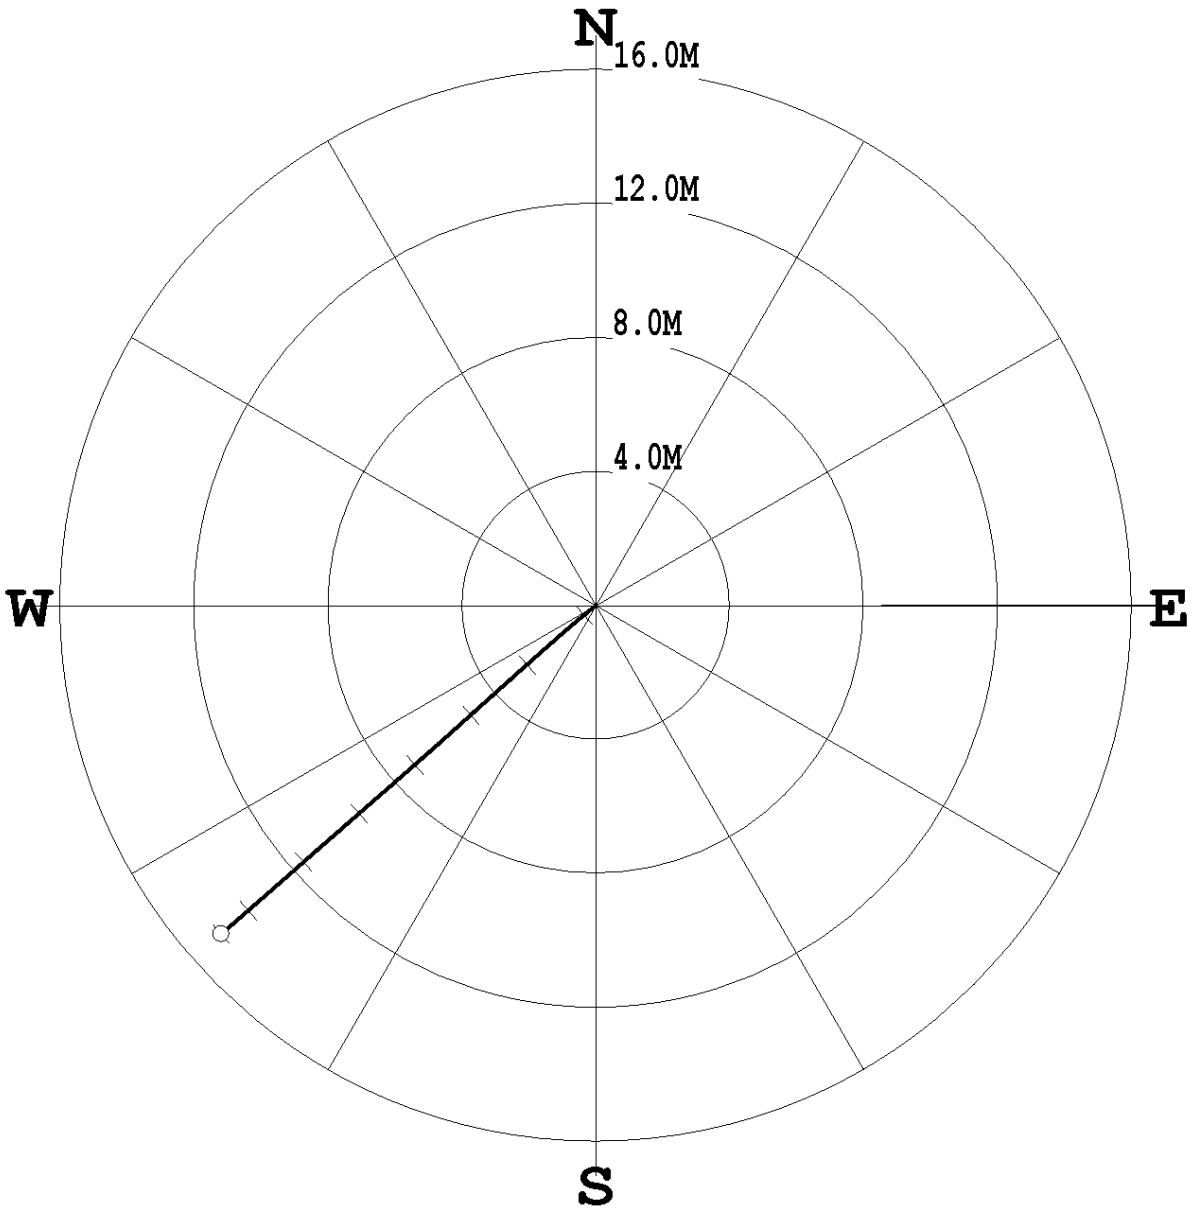

* * * * * * * COMPU-LOG - VERTICAL DEVIATION * * * * * * *

CLIENT : ATRUM COAL
FIELD OFFICE : CENTURY GEO
DATA FROM : N/A
MAG. DECL. : 19.500
LOG: DHGH-14-20_06-24-14_05-32_9411A_005_14.00_50.58_DEVI.log

HOLE ID. : DHGH-14-20
DATE OF LOG : 06/24/14
PROBE : 9411A , 4504
DEPTH UNITS : METERS

CABLE DEPTH	TRUE DEPTH	NORTH DEV.	EAST DEV.	DISTANCE	AZIMUTH	SANG	SANGB
14.01	14.00	-0.00	-0.00	0.0	234.0	24.4	234.0
15.00	14.91	-0.25	-0.32	0.4	232.0	24.3	231.2
16.00	15.82	-0.52	-0.64	0.8	231.0	24.3	229.6
17.00	16.73	-0.79	-0.95	1.2	230.4	24.3	229.1
18.00	17.64	-1.06	-1.26	1.6	230.1	24.2	228.4
19.00	18.56	-1.33	-1.57	2.1	229.8	24.3	228.6
20.00	19.47	-1.60	-1.88	2.5	229.5	24.3	228.5
21.00	20.38	-1.87	-2.19	2.9	229.4	24.3	228.4
22.00	21.29	-2.15	-2.49	3.3	229.2	24.3	228.0
23.00	22.20	-2.42	-2.80	3.7	229.1	24.2	228.3
24.00	23.12	-2.70	-3.11	4.1	229.0	24.2	227.9
25.00	24.03	-2.97	-3.41	4.5	229.0	24.2	227.9
26.00	24.94	-3.24	-3.72	4.9	228.9	24.2	228.1
27.00	25.85	-3.52	-4.02	5.3	228.8	24.3	228.1
28.00	26.76	-3.79	-4.33	5.8	228.8	24.2	228.1
29.00	27.68	-4.06	-4.63	6.2	228.7	24.1	228.2
30.00	28.59	-4.33	-4.94	6.6	228.7	24.0	228.4
31.00	29.50	-4.60	-5.24	7.0	228.7	24.0	228.5
32.00	30.42	-4.87	-5.55	7.4	228.7	23.9	228.9
33.00	31.33	-5.14	-5.85	7.8	228.7	23.9	228.5
34.00	32.25	-5.40	-6.15	8.2	228.7	23.8	228.9
35.00	33.16	-5.67	-6.46	8.6	228.7	23.8	229.0
36.00	34.08	-5.93	-6.76	9.0	228.7	23.7	228.9
37.00	34.99	-6.20	-7.07	9.4	228.8	23.7	228.8
38.00	35.91	-6.46	-7.37	9.8	228.8	23.7	228.8
39.00	36.82	-6.72	-7.67	10.2	228.8	23.7	228.9
40.00	37.74	-6.99	-7.97	10.6	228.8	23.8	228.9
41.00	38.65	-7.25	-8.28	11.0	228.8	23.7	228.5
42.00	39.57	-7.52	-8.58	11.4	228.8	23.8	228.7
43.00	40.48	-7.79	-8.88	11.8	228.8	23.7	228.6
44.00	41.40	-8.05	-9.18	12.2	228.8	23.7	228.9
45.00	42.32	-8.32	-9.49	12.6	228.8	23.7	228.6
46.00	43.23	-8.58	-9.79	13.0	228.8	23.7	228.9
47.00	44.15	-8.85	-10.09	13.4	228.8	23.7	228.6
48.00	45.06	-9.11	-10.39	13.8	228.8	23.7	228.7
49.00	45.98	-9.37	-10.70	14.2	228.8	23.7	228.9
50.00	46.89	-9.64	-11.00	14.6	228.8	23.7	229.4
50.58	47.42	-9.79	-11.17	14.9	228.8	23.7	228.9
